

Detour for Phase 1:

Detour To Hospital Main Entrance


Detour To Employee Lot, Physician Lot, Loading Dock, and Emergency Room

Phase 1:

- paint striping
- paint arrows at stoplight
- paint stop bars
- paint crosswalks

Scope: from Stoplight at South Entrance to Front Entrance and from 4-way stop to Med Imaging Lot Entrance on Campus Loop Road

Timeframe: Thursday Morning (may be pushed back if rain exists)

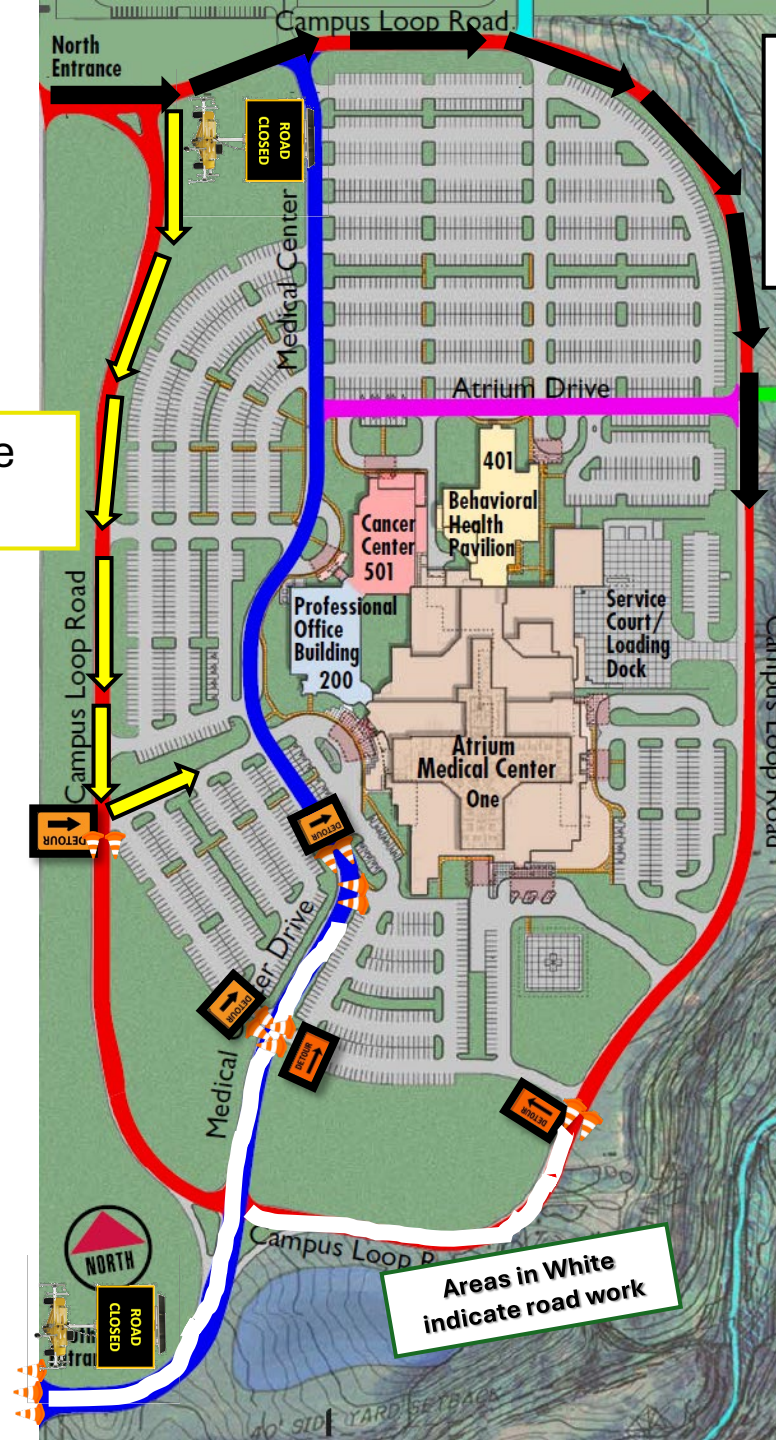


Detour for Phase 2:

Emergency vehicle detour for this phase on next page

Detour To Hospital Main Entrance

Signage will indicate hospital traffic turn left, emergency vehicles proceed straight

Keeping this entrance closed to force public traffic to north entrance to get to ETC

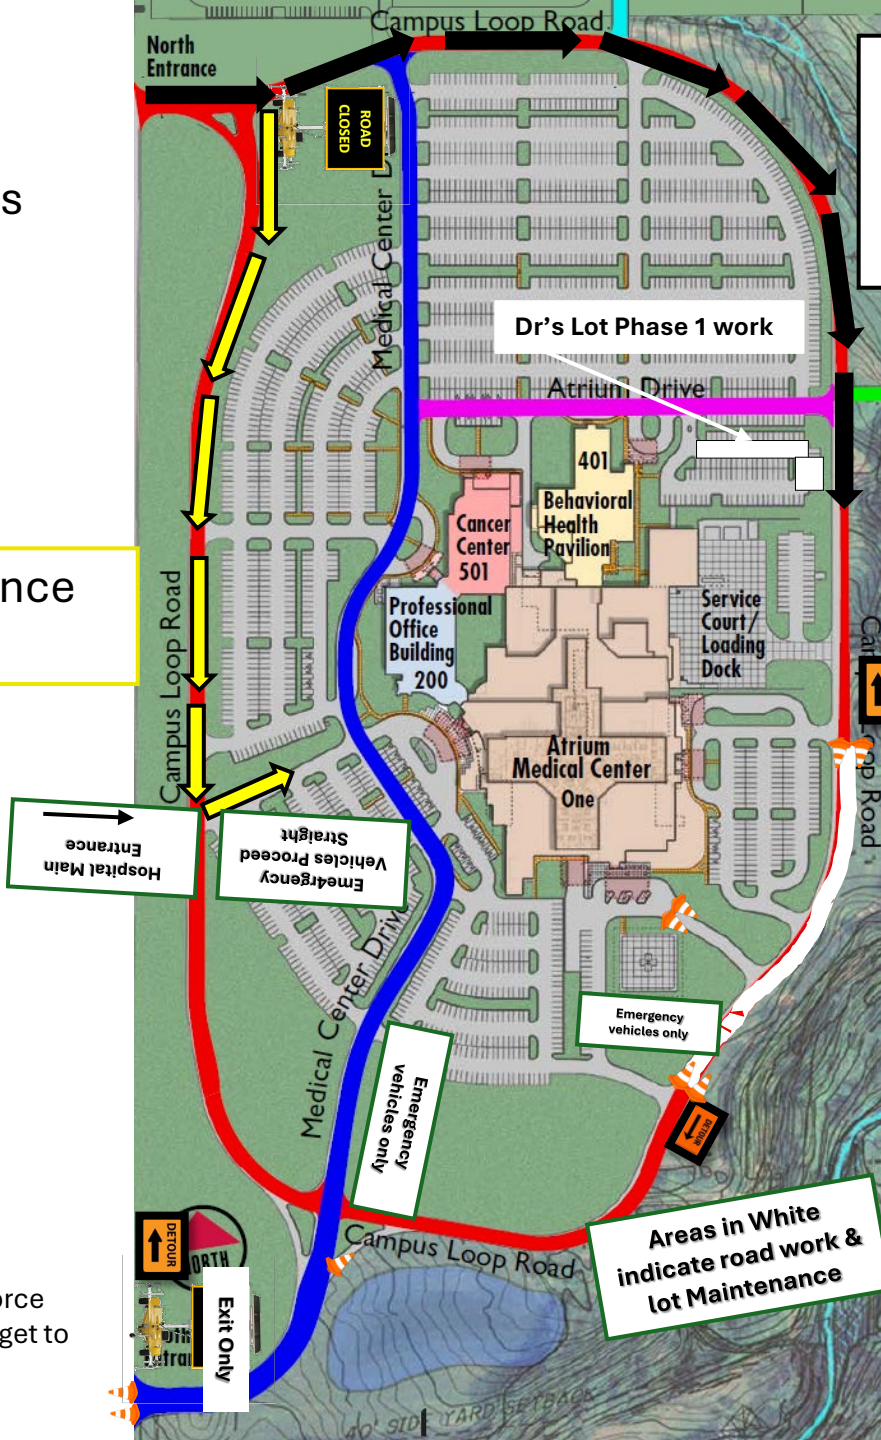

Detour To Employee Lot, Physician Lot, Loading Dock, and Emergency Room

Phase 2:

- paint striping
- paint crosswalks
- Pothole repair

Scope: From Med Imaging Lot Entrance to E.R. Entrance

Start Dr.'s Lot Phase 1 crack sealing and stripe parking spaces


Timeframe: Thursday Afternoon (may be pushed back if rain exists)

Emergency Vehicle Detour for Phase 2:

For this phase only. For all other phases emergency vehicles will follow posted detour routes

Signage will indicate hospital traffic turn left, emergency vehicles proceed straight

Keeping this entrance closed to force public traffic to north entrance to get to ETC. EMS will have access to their area

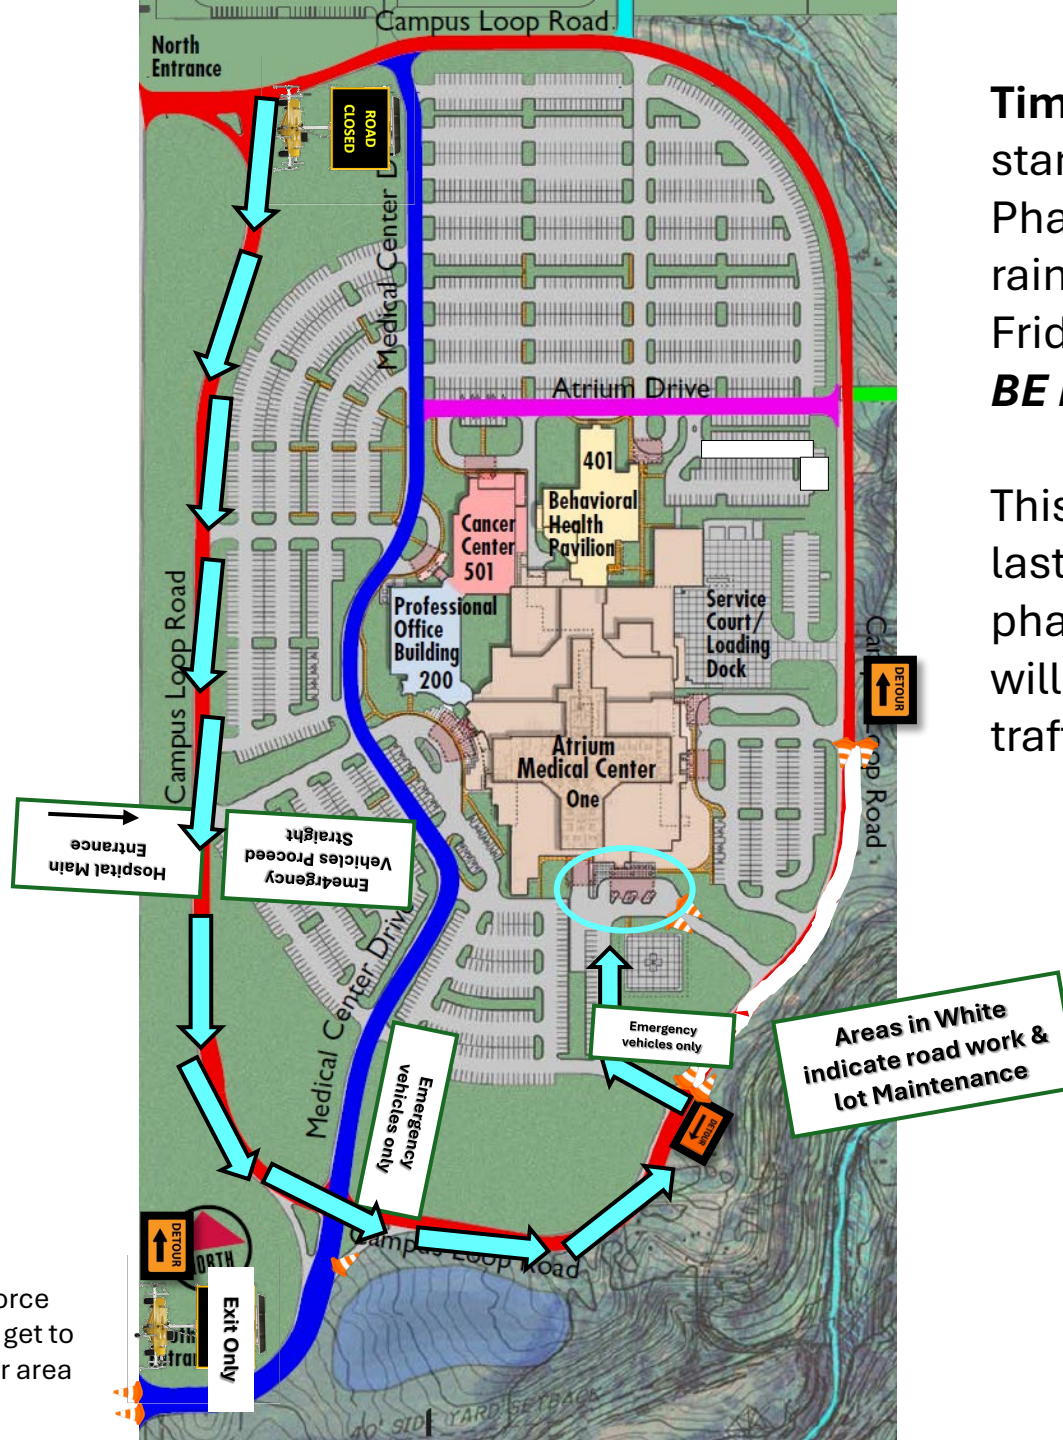

Timeframe: Work is expected to start Thursday Afternoon (after Phase 1 paint / patch is dry). (If rain exists may be pushed to Friday morning). ***SIGNAGE WILL BE PRESENT TO DIRECT YOU.***

This closure is only expected to last a couple hours. Once this phase is done, the South Entrance will be opened back up for all traffic.


Detour for Phase 3:

Phase 3:


- paint striping from North Entrance to entrance of MCHC
- paint crosswalks, stop bars, and arrows at North Entrance
- Pothole repair
- Also includes Part of Doctor's Lot crack sealing and stripe parking spaces

Scope: From North Entrance to driveway of 100-200 Medical Center Dr. (leaving driveway open)

Timeframe: Friday Morning (may be pushed back if rain delays exist)

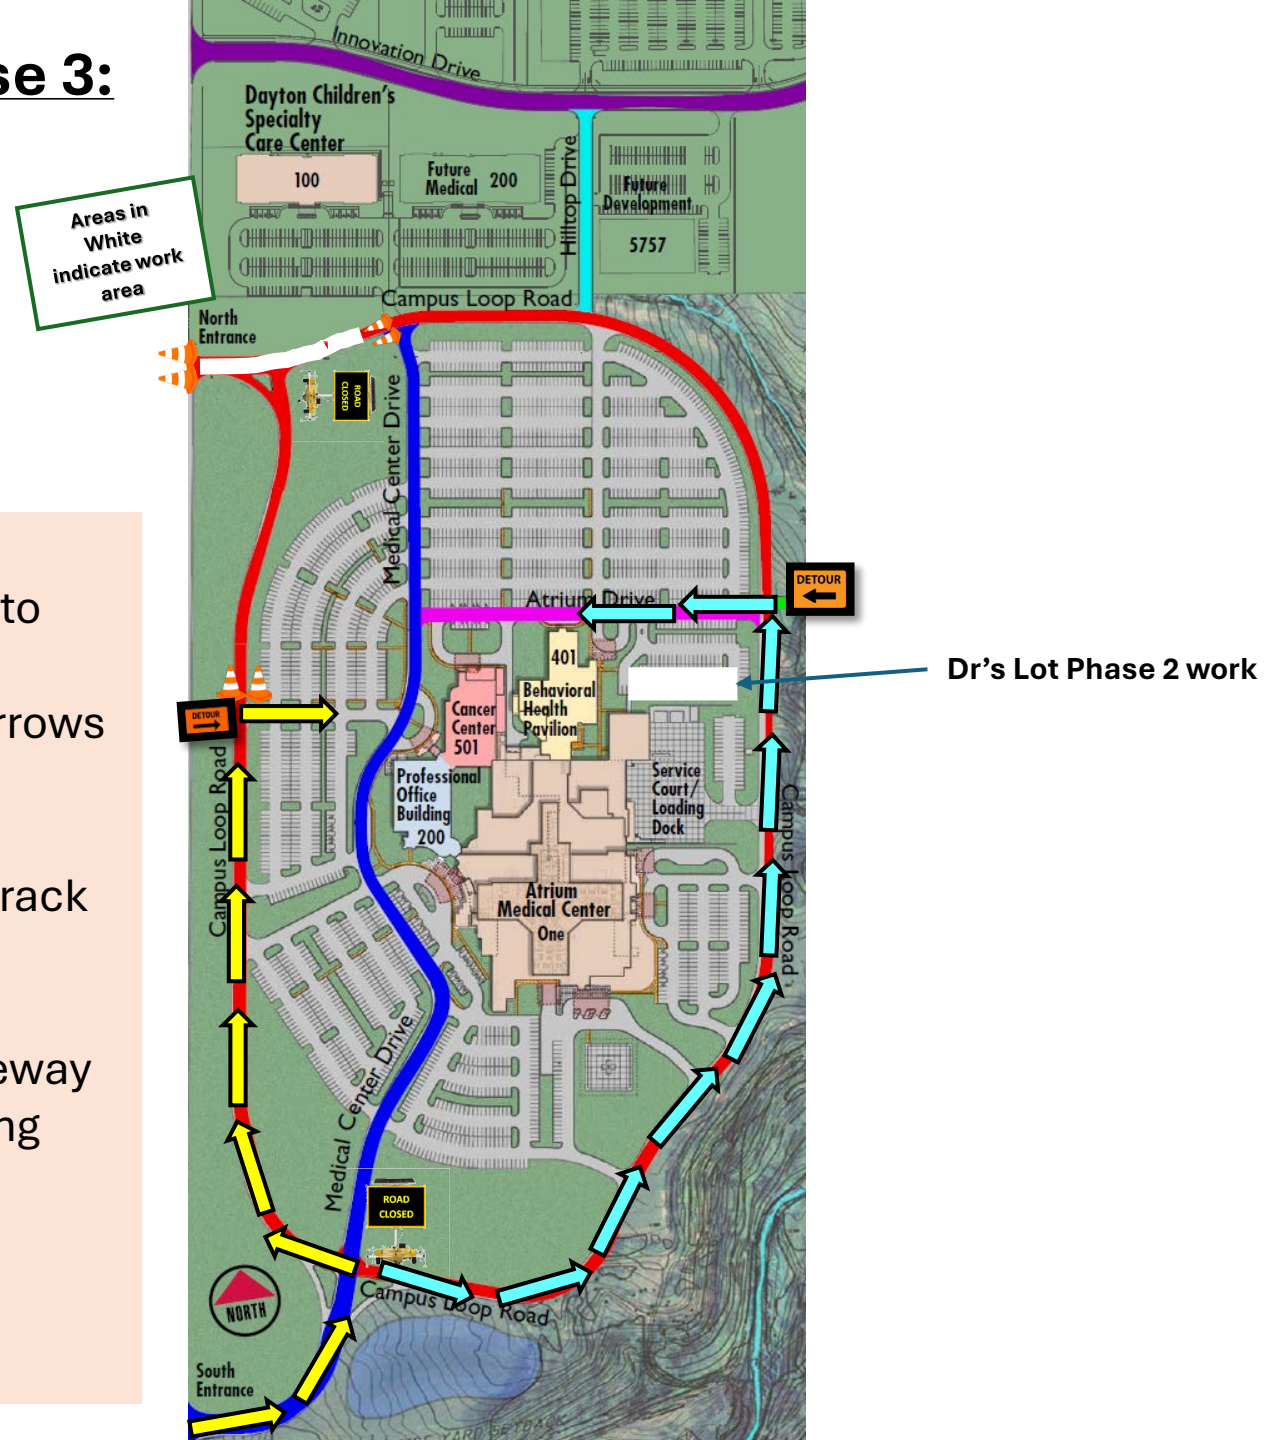

Detour for Phase 3 for 100 and 200 Campus Loop Rd (100-200 Campus Loop Rd):

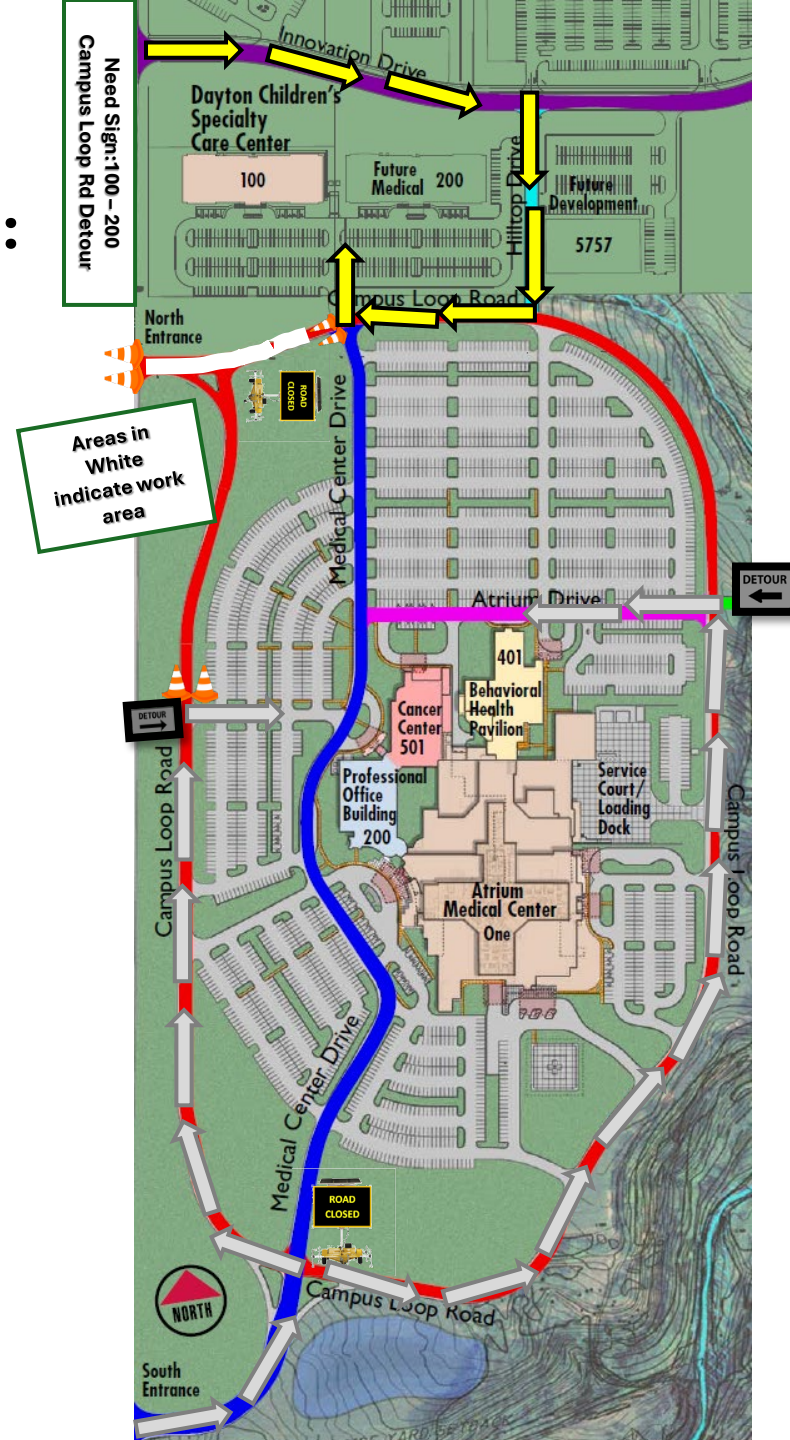

Detour for Phase 4:

Phase 4:

- paint striping, crosswalks, pothole repair from MCHC Entrance to Hilltop Dr.
- Also includes other portion of Doctor's Lot crack sealing and stripe parking spaces

Scope: from driveway of 100-200 Campus Loop Rd to Hilltop Dr.

Timeframe: Friday Afternoon (may be pushed to Monday if rain exists)

